

Desktop survey undertaken from google street view with imagery

All traffic management shall comply with all current legislation and guidance including Chapter 8, Safety at Street Works and Road Works (A Code of Practice).

Pedestrian management to be installed and managed to suit site conditions in accordance with current legislation & codes of practice by the contractor unless otherwise stated.

All signage and road markings shall conform with the Traffic Signs

Sign locations are indicative only, exact location to be determined on site.

Suitably qualified operative to assess site to ensure the installation complies with all current legislation. Any issues and/or changes from the original design should be immediately reported to the relevant contracts

This design is only valid for 12months from date of production and should be re-evaluated if installation is to take place after this period.

SIGN SCHEDULE	De Brid
Qty: 4 Ref: 13.9 Schedule 13-9 : Temporary Information	Road closed This isostion may be recorded for compliance purposes
Qty: 2 Ref: 13.9 Schedule 13-9 : Temporary Information	Diversion
Oly: 1 Ref: 2702 Start of temporary diversion route	Diversion
Oty: 2 Ref: 2702 End of temporary diversion route	Diversion ENDS
Qty: 1 Ref: 2702 Start of temporary diversion route	Diversion
Oly: 1 Ref: 2702 Start of temporary diversion route	Diversion -
Oty: 2 Ref: 2703 Direction of temporary diversion route from junction ahead	Diverte traffic
Qty: 1 Ref: 2703 Direction of temporary diversion route from junction ahead	Diverted
Qty: 1 Ref: 2703 Direction of temporary diversion route from junction ahead	← Divert traffi
Oty: 1 Ref: 2703 Direction of temporary diversion route u-turn at roundabout ahead	Diverted traffic
Oly: 7 Ref. 2704 Direction of temporary diversion route	Diverto
Qty: 1 Ref: 2704 Direction of temporary diversion route	Diverted traffic
Qty: 1 Ref: 2706 Roundabout ahead leading to temporary diversion route	Diverted traffic
Qty: 1 Ref: 2706 Roundabout ahead leading to temporary diversion route	Diverte
Oty: 2 Ref: 573 Direction to hazard right	-
Oty: 2 Ref: 573 Direction to hazard left	—
Oly: 7 Ref: 7001 Road works ahead	₽
Oty: 6 Ref: 7010-FP-13-9 Nature of temporary hazard ahead - Road Ahead Closed	ROAD AHEAD CLOSED
Qty: 4 Ref: 7010-FP-13-9 Nature of temporary hazard ahead - Road Closed	ROAD CLOSED


AWS signage installed at least 2 weeks prior to works commencing. Dates & durations to be confirmed.


Parked vehicles/parking bays are present and could interfere with the works. No parking cones are to be installed prior to works commencing with appropriate signage if required.

1	Key:			
		Works Area		Temporary Traffic Signal
		Closure	R	Stop & Go Board
		Vehicular Diversion Route		Temporary Ped Signal
	- ⊁-	Ped Diversion Route	•	Existing Bus Stop
	•	Cone	•	Temporary Sign
	•	Datum Point	+-+	Pedestrian Barrier

Safety information:	
lin width of sideways safety zone (S)	0.5m
lin length of longways clearance (L)	0.5m
alph Road	30

Site information:							
NSG	Ralph Road, Shirley Solihill						
Local Authority	Solihull						
USRN	35005307						
Road Type	Single lane carriageway Road Width Varies		3				
Works Location	X:412333 Y:279760						
Surveyed	X	Bus Stop(s))	(Parked Ve	hicles	✓
Perm Signals	X	Controlled Crossing)	(Cycle Lan	es	X

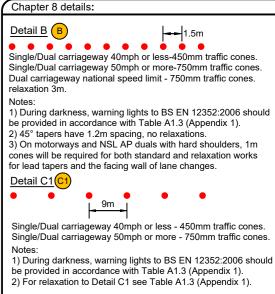



Single carriageway 40mph or less - 450mm traffic cones. Single/Dual carriageway 50mph or more - 750mm traffic cones.

1) During darkness, warning lights to BS EN 12352:2006 should be provided in accordance with Table A1.3.



total traffic & event management solutions Old Arden Brickworks | Bickenhill | Solihull | West Midlands | B92 0DY t +44 (0)800 819 9001 | f +44 (0)1675 442507 info@traffixuk.com | www.traffixuk.com

Project title:						
,	Traffic Management					
Ralph Road	Proposed Road Closure					
Solihull B90 3JZ	1					
Date: 05/09/2025	Scale: NTS	Paper: A2				
Drawn: CM	Checked: BN	Approved: MT				
Project Number: TFX MT3259	Drawing Number: 001	Revision:				

This drawing is copyright & the property of Traffix & must not be copied in whole or in part without their written permi This drawing must not be scaled.

The Contractor is to report all discrepancies & errors to the Contract Manage
