


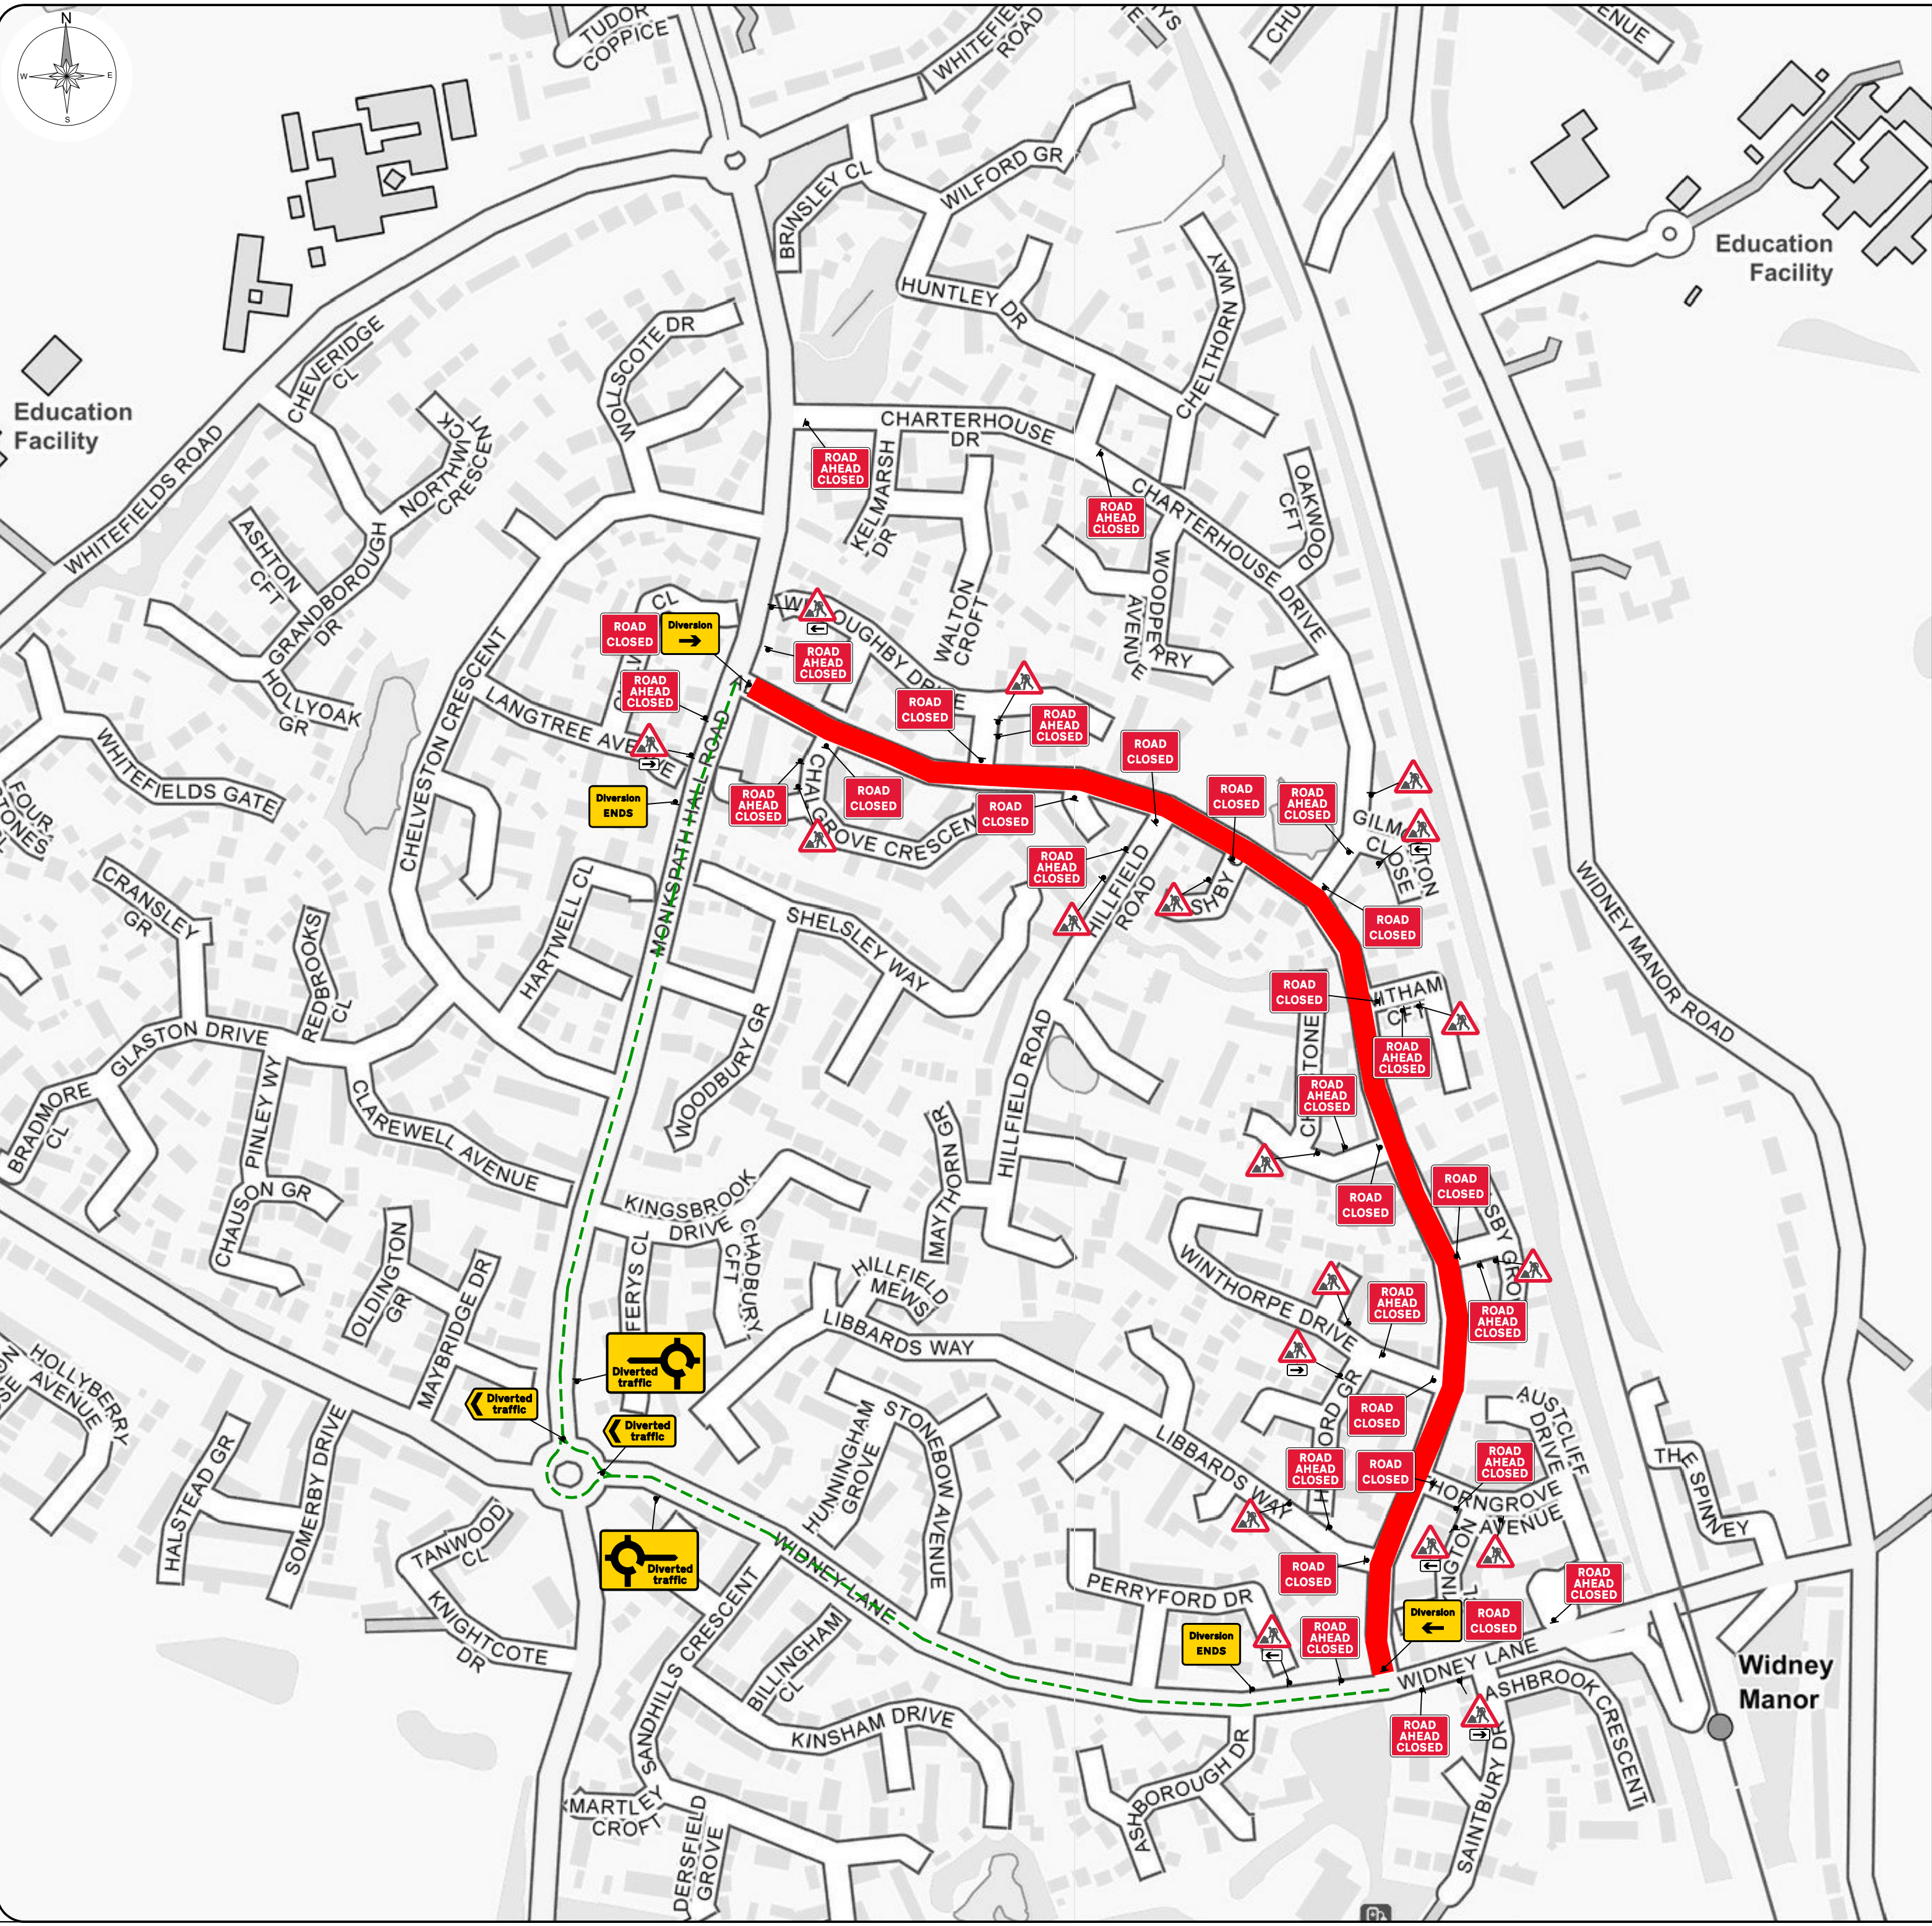

Desktop survey undertaken from google street view with imagery dated: -

All traffic management shall comply with all current legislation and guidance including Chapter 8, Safety at Street Works and Road Works (A Code of Practice).

Pedestrian management to be installed and managed to suit site conditions in accordance with current legislation & codes of practice by the contractor unless otherwise stated.

All signage and road markings shall conform with the Traffic Signs Regulations and General Directions (TSRGD).

Sign locations are indicative only, exact location to be determined on site.

Suitably qualified operative to assess site to ensure the installation complies with all current legislation. Any issues and/or changes from the original design should be immediately reported to the relevant contracts manager/designer.

This design is only valid for 12months from date of production and should be re-evaluated if installation is to take place after this period.

SIGN SCHEDULE		
Qty: 1 Ref: 2702 Start of temporary diversion route		
Qty: 2 Ref: 2702 End of temporary diversion route		
Qty: 1 Ref: 2702 Start of temporary diversion route		
Qty: 2 Ref: 2704 Direction of temporary diversion route		
Qty: 1 Ref: 2706 Roundabout ahead leading to temporary diversion route		
Qty: 1 Ref: 2706 Roundabout ahead leading to temporary diversion route		
Qty: 4 Ref: 573 Direction to hazard left		
Qty: 3 Ref: 573 Direction to hazard right		
Qty: 18 Ref: 7001 Road works ahead		
Qty: 17 Ref: 7010-FP-13-9 Nature of temporary hazard ahead - Road Ahead Closed		
Qty: 14 Ref: 7010-FP-13-9 Nature of temporary hazard ahead - Road Closed		

Key:			
	Works Area		Temporary Traffic Signal
	Closure		Stop & Go Board
	Vehicular Diversion Route		Temporary Ped Signal
	Ped Diversion Route		Existing Bus Stop
	Cone		Temporary Sign
	Datum Point		Pedestrian Barrier

Safety information:	
Min width of sideways safety zone (S)	
Min length of longways clearance (L)	

Site information:			
NSG	ALDERMINSTER ROAD, HILLFIELD, SOLIHULL		
Local Authority	SOLIHULL		
USRN	35004965		
Road Type	Single lane carriageway	Road Width	xx.xxm
Works Location	X:415217	Y:278035	
Surveyed	☒ Bus Stop(s)	Parked Vehicles	
Perm Signals	☐ Controlled Crossing	Cycle Lanes	

Chapter 8 details:

Detail B

Single/Dual carriageway 40mph or less-450mm traffic cones. Single/Dual carriageway 50mph or more-750mm traffic cones. Dual carriageway national speed limit - 750mm traffic cones. relaxation 3m.

Notes:

- 1) During darkness, warning lights to BS EN 12352:2006 should be provided in accordance with Table A1.3 (Appendix 1).
- 2) 45° tapers have 1.2m spacing, no relaxations.
- 3) On motorways and NSL AP duals with hard shoulders, 1m cones will be required for both standard and relaxation works for lead tapers and the facing wall of lane changes.

Detail C1

Single/Dual carriageway 40mph or less - 450mm traffic cones. Single/Dual carriageway 50mph or more - 750mm traffic cones.

Notes:

- 1) During darkness, warning lights to BS EN 12352:2006 should be provided in accordance with Table A1.3 (Appendix 1).
- 2) For relaxation to Detail C1 see Table A1.3 (Appendix 1).

Detail C2

Single carriageway 40mph or less - 450mm traffic cones. Single/Dual carriageway 50mph or more - 750mm traffic cones.

Notes:

- 1) During darkness, warning lights to BS EN 12352:2006 should be provided in accordance with Table A1.3.

Rev	Date	Comments	By	Chk

Balfour Beatty
Living Places
Working in Partnership with
traffix
total traffic & event management solutions
Old Arden Brickworks | Bickenhill | Solihull |West Midlands | B92 0DY
t +44 (0)800 819 9001 | f +44 (0)1675 442507
info@traffixuk.com | www.traffixuk.com

Project title: Traffic Management		
Drawing title: Proposed Road Closure Alderminster Road Solihull B91 3YU		
Date: 27/03/2026	Scale: NTS	Paper: A2
Drawn: BN	Checked: CM	Approved: MT
Project Number: TFX MT3415	Drawing Number: 001	Revision: -

This drawing is copyright & the property of Traffix & must not be copied in whole or in part without their written permission. Copyright is reserved. © This drawing must not be scaled.
The Contractor is to report all discrepancies & errors to the Contract Manager prior to works commencing.
