


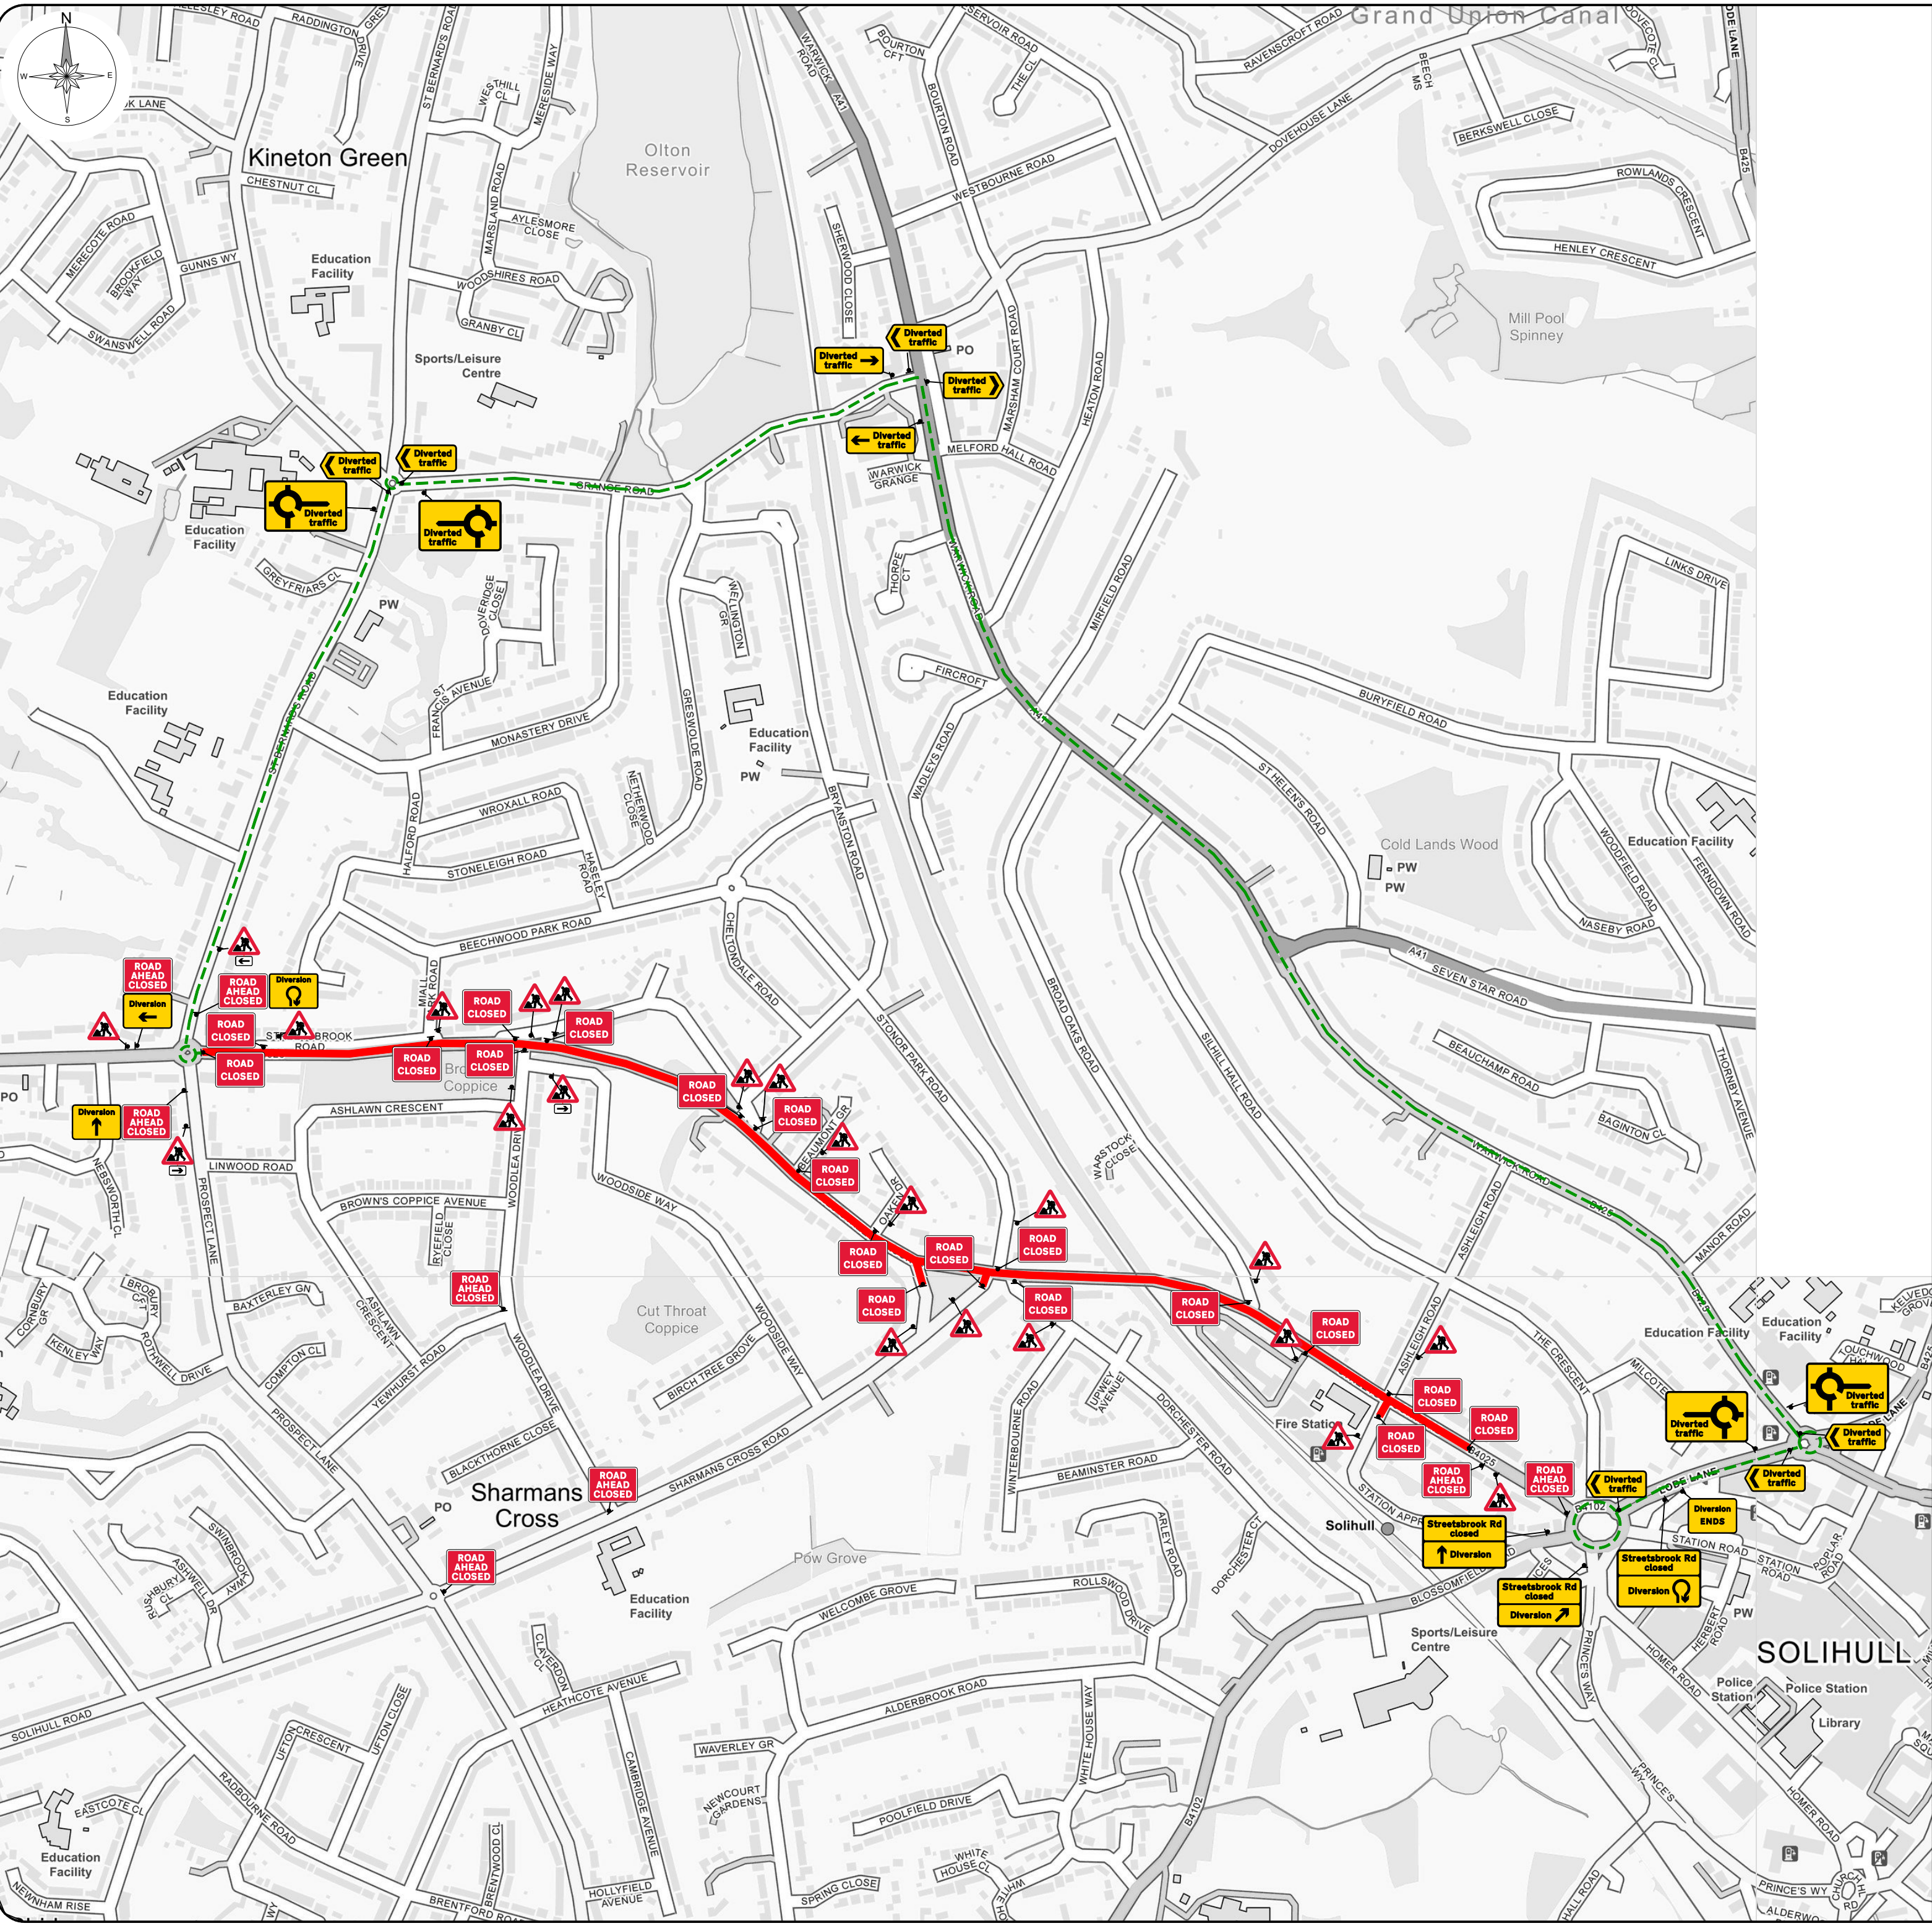

Desktop survey undertaken from google street view with imagery dated: July 2024

All traffic management shall comply with all current legislation and guidance including Chapter 8, Safety at Street Works and Road Works (A Code of Practice).

Pedestrian management to be installed and managed to suit site conditions in accordance with current legislation & codes of practice by the contractor unless otherwise stated.

All signage and road markings shall conform with the Traffic Signs Regulations and General Directions (TSRGD).

Sign locations are indicative only, exact location to be determined on site.

Suitably qualified operative to assess site to ensure the installation complies with all current legislation. Any issues and/or changes from the original design should be immediately reported to the relevant contracts manager/designer.

This design is only valid for 12months from date of production and should be re-evaluated if installation is to take place after this period.

Size of signage:		
Single carriageway permanent speed limit as shown below or less)		
30	40	50 or more
600mm	750mm	900mm

SIGN SCHEDULE	
Qty: 1 Ref: 13.9 Schedule 13-9: Temporary Information	
Qty: 1 Ref: 13.9 Schedule 13-9: Temporary Information	
Qty: 1 Ref: 13.9 Schedule 13-9: Temporary Information	
Qty: 1 Ref: 13.9 Schedule 13-9: Temporary Information	
Qty: 1 Ref: 2702 Start of temporary diversion route	
Qty: 1 Ref: 2702 Start of temporary diversion route	
Qty: 1 Ref: 2702 End of temporary diversion route	
Qty: 1 Ref: 2702 End of temporary diversion route	
Qty: 1 Ref: 2703 Direction of temporary diversion route from junction ahead	
Qty: 1 Ref: 2703 Direction of temporary diversion route from junction ahead	
Qty: 8 Ref: 2704 Direction of temporary diversion route	
Qty: 1 Ref: 2704 Direction of temporary diversion route	
Qty: 2 Ref: 2706 Roundabout ahead leading to temporary diversion route	
Qty: 2 Ref: 2706 Roundabout ahead leading to temporary diversion route	
Qty: 1 Ref: 573 Direction to hazard left	
Qty: 2 Ref: 573 Direction to hazard right	
Qty: 22 Ref: 7001 Road works ahead	
Qty: 8 Ref: 7010-FP-13.6 Nature of temporary hazard ahead - Road Ahead Closed	
Qty: 19 Ref: 7010-FP-13.6 Nature of temporary hazard ahead - Road Closed	

Key:			
	Works Area		Temporary Traffic Signal
	Closure		Stop & Go Board
	Vehicular Diversion Route		Temporary Ped Signal
	Ped Diversion Route		Existing Bus Stop
	Cone		Temporary Sign
	Datum Point		Pedestrian Barrier

Safety information:	
Min width of sideways safety zone (S)	0.5m
Min length of longways clearance (L)	0.5m
Streetsbrook Road	30

Site information:				
NSG	Streetsbrook Road, Solihull			
Local Authority	Solihull MBC			
USRN	35010036			
Road Type	Single lane carriageway		Road Width	Varies
Works Location	X:412252		Y:280199	
Surveyed	✗	Bus Stop(s)	✓	Parked Vehicles
Perm Signals	✗	Controlled Crossing	✗	Cycle Lanes
				✗

Chapter 8 details:

Detail B

Detail C1

Detail C2

Rev	Date	Comments	By	Chk

Balfour Beatty
Living Places
Working in Partnership with
traffix
total traffic & event management solutions
Old Arden Brickworks | Bickenhill | Solihull | West Midlands | B92 0DY
t +44 (0)800 819 9001 | f +44 (0)1675 442507
info@traffixuk.com | www.traffixuk.com

Project title: Traffic Management		
Drawing title: Proposed Road Closure Streetsbrook Road Solihull B90 3LX		
Date: 30/06/2026	Scale: NTS	Paper: A2
Drawn: LO	Checked: MO	Approved: MT
Project Number: TFX MT3516	Drawing Number: 001	Revision: -

This drawing is copyright & the property of Traffix & must not be copied in whole or in part without their written permission. Copyright is reserved. © This drawing must not be scaled.
The Contractor is to report all discrepancies & errors to the Contract Manager prior to works commencing.

AWS signage installed at least 2 weeks prior to works commencing. Dates & durations to be confirmed.
